

Kendal Flood Risk Management Scheme

Gooseholme in-river works – Week Commencing 21st September 2026



Flood defence wall near completion following the huge engineering task of the sewer and Stock Beck diversions and the construction of the 9 x 6 metre wet well under ground




The stone cladding on the outfall and revetment is progressing and working up the banked area

Progress Update

In-river works are due to be completed this week, marking an important milestone for the project. This will allow the team to continue demobilising the work area, including the removal of pumping equipment, machinery and materials used to carry out the in-river and masonry works. Recent rainfall and higher river levels have impacted progress on the lower section of the stone cladding at the Stock Beck outfall structure. The stone masons have continued working and the structure is now in its final stages of completion.

Kendal Flood Risk Management Scheme

Gooseholme reinstatement and phased completion plan

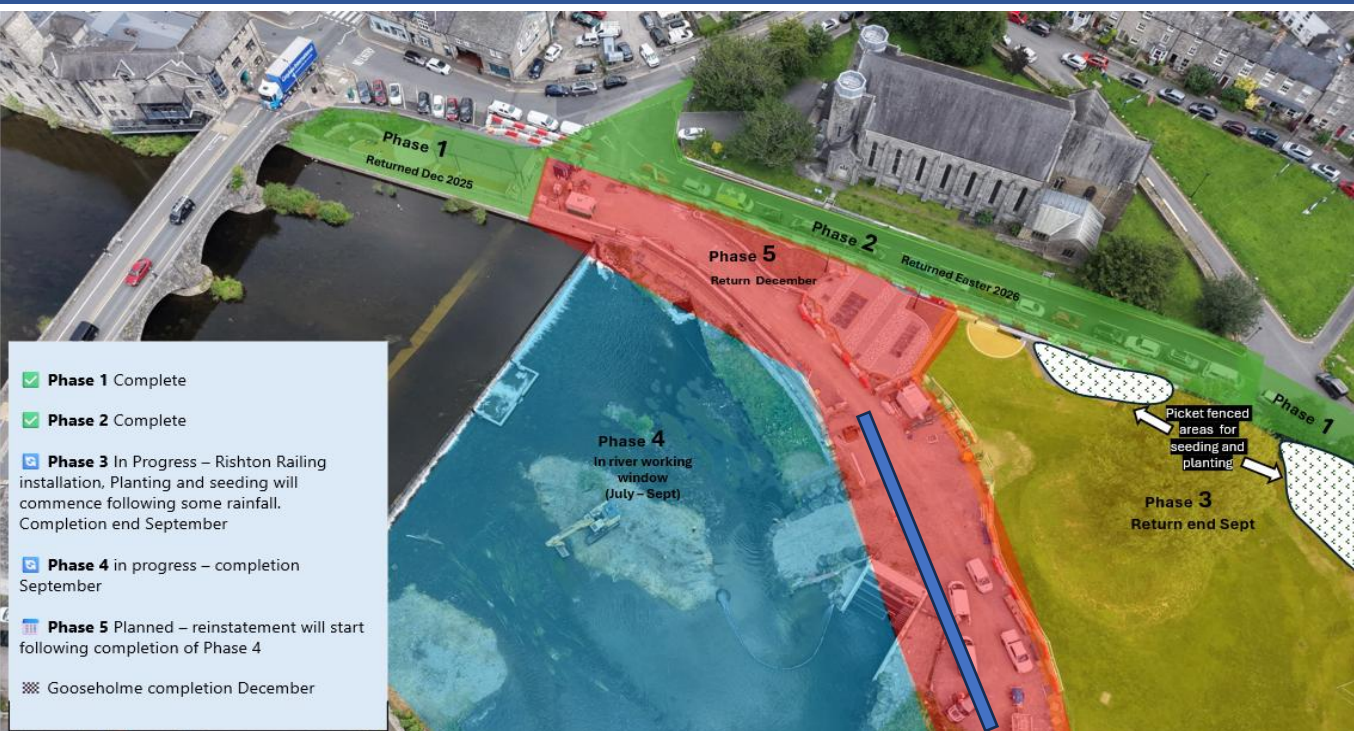

The re-instatement works continue replacing kerb stones ready for the path to be prepared and tarmacked

We are taking a phased approach to completing areas of Gooseholme common with the next area for completion being Phase 3 (yellow area).

Works will continue this week to reinstate the riverside footpath that leads from Gooseholme Bridge through the Common. Reinstatement works have started downstream of the new Stock Beck outfall and work towards Castle street. These works are part of the reinstatement of this section as we complete construction, and our in-river works within this area.
